
AIMOC WIM

03 - Static inbound + static outbound

CONFIDENTIAL - CONCEPT

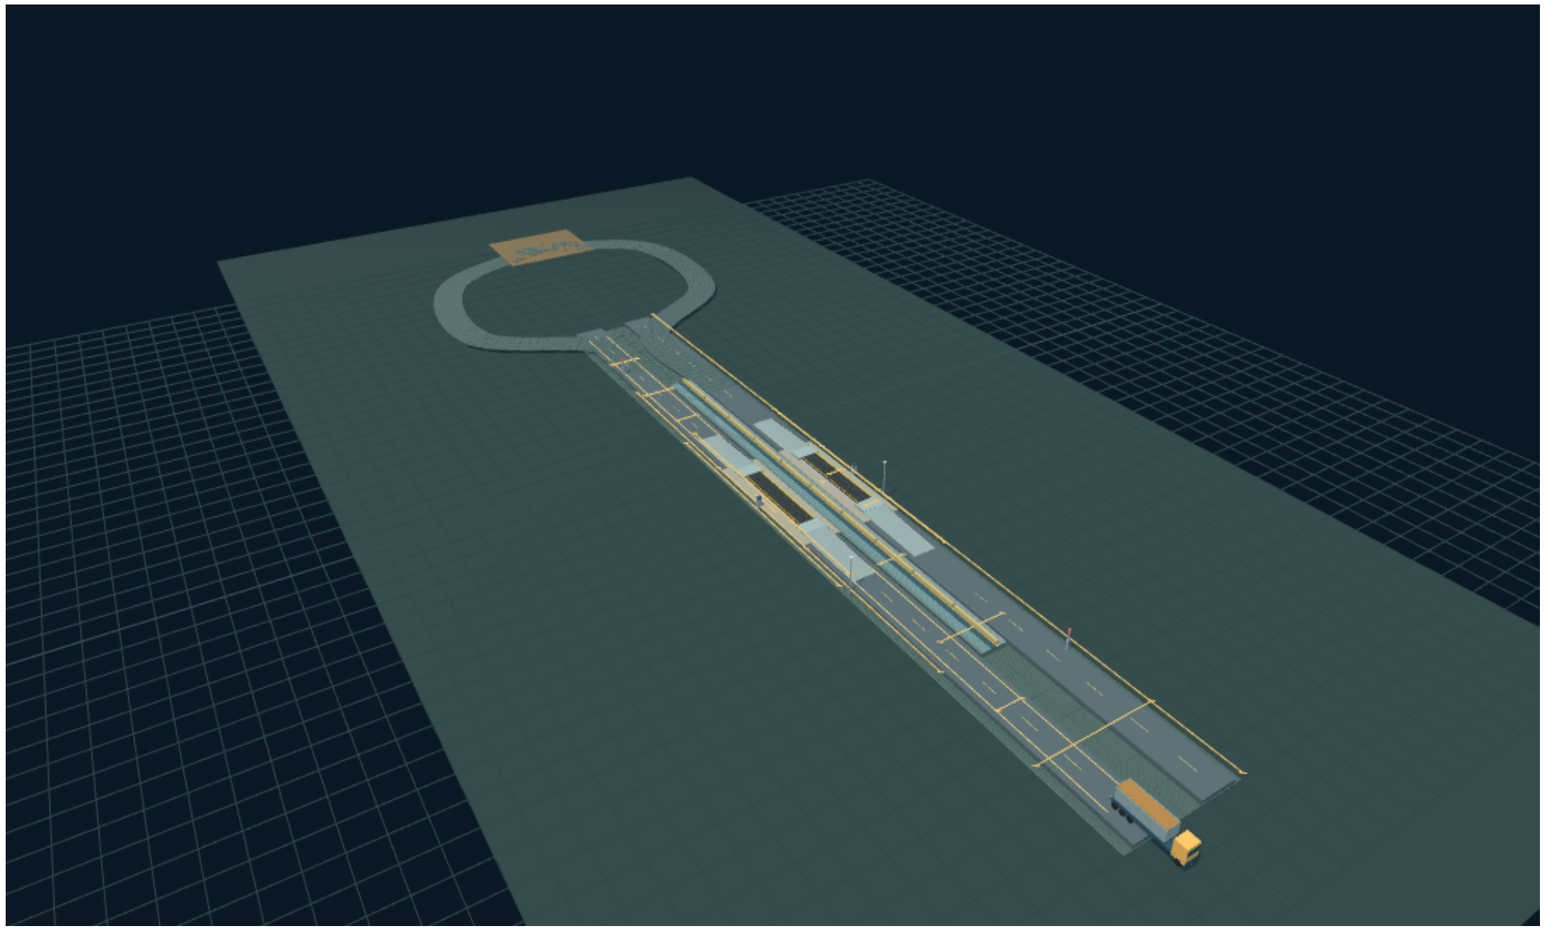

Modular static: 80 t x 20 kg; pitless modular

Platform 18 x 3 m; drawing overall width 3.20 m

6 modules: 1.50 x 6.00 x 0.308 m each

Two stations: each 8 x 30 t cells / FS-8000

Static deck +1.608 m; rise 0.708 m*

Ramps 2 x 14.16 m @ 5%; footprint 52.32 m*

Two static stations; no WIM / quartz / WIM IR

Working corridor 22 x 170 m; centres 12.5 m

*Levels, ramps, landings and raft are coordination assumptions; the PDF does not supply foundation drawings. 3.2 m is an overall dimension, not clear width.

3.2 m trucks are held for tyre/rail review. Gross above 80 t produces no final weight. QR does not replace position detection.

Source: customer-supplied technical PDF, pages 3-9. Quoted prices and personal contacts are not published.

PDF specifications are distinguished from civil assumptions. Not OEM construction drawings.

Component	Specification	Source note
Type / capacity	Pitless modular movable · 80 t × 20 kg	PDF p. 8
Nominal platform / drawing overall width	18 × 3 m / 3.20 m	PDF p. 4, 8 · bukan lebar bersih / not clear width
Modules / arrangement	6 × (1.50 × 6.00 × 0.308 m) · 2 across × 3 longitudinal	PDF p. 4, 8
Structure / surface	L-Series steel · chequered steel deck	PDF p. 5 · 308 mm = module depth, not plate gauge
Guard rails / each	12 × (75 × 2900 × 180 mm)	PDF p. 4, 8
Finish	Sandblasting + 2-tone heavy-duty powder coating 300 um; black platform / yellow rails	PDF p. 3, 8
Load cells / mounts	8 × Balanza LX8 30 t analog + 8 mounts	PDF p. 7-8 · scale stays 80 t, not 240 t
Indicator	Fine FS-8000 · Korean · table/panel · 7-digit blue display · aluminium housing	PDF p. 7-8
Indicator features	Auto span calibration; push-button/auto tare; peak/sample hold; M+/M-; claimed 10-year data backup	PDF p. 7 · modes/retention to verify

PDF specifications are distinguished from civil assumptions. Not OEM construction drawings.

Component	Specification	Source note
Junction / cabling / surge	1 × 8-channel stainless junction box; 8 cable thyristor items; 25 m load-cell cable; 1 surge protection	PDF p. 7-8 · cable thyristor term requires clarification
Cell specifications	Combined error ±0.03% F.S.; zero balance ±1% F.S.; insulation 5000 Mohm; operating -20...+70°C	PDF p. 7 · cell specs, not whole-scale accuracy
Sensitivity / cell overload	PDF: 2.0 ±0.002%mV/V; safe load 150% F.S.; ultimate 200% F.S.	PDF p. 7 · sensitivity notation requires clarification; not operating permission
Cell protection	PDF lists IP67 (5 t), IP68 (10-15 t); 30 t rating NOT specified	PDF p. 7 · no IP68 claim for quoted 30 t cells
Cell material	Alloy steel / stainless steel listed; selected variant unconfirmed	PDF p. 7 · confirm coastal corrosion grade
Local software	CALISTA / Callista standard: single/double weighing, multilevel access, ticket customisation, Excel export, reports	PDF p. 7-8 · spelling differs; not a confirmed API
Calibration accessories	5 × 20 kg test weights listed; not sufficient by themselves for full 80 t verification	PDF p. 8 · authority/OEM test-load plan needed
Fabrication / installation	30 days after PO if unavailable; on-site installation 4 working days	PDF p. 9 · not total civil / commissioning duration
Warranty / metrology	Electronics 1 year; structure 3 years, conditional; type approval claimed, certificate not supplied	PDF p. 6, 9 · verify exact approval and site tera


PDF specifications are distinguished from civil assumptions. Not OEM construction drawings.

PLAN · TWO STATIC STATIONS



*Coordination: two 28 × 7.5 m rafts; two 52.32 m footprints; loop/holding excluded.

SECTION · TWO SEPARATE FOUNDATIONS

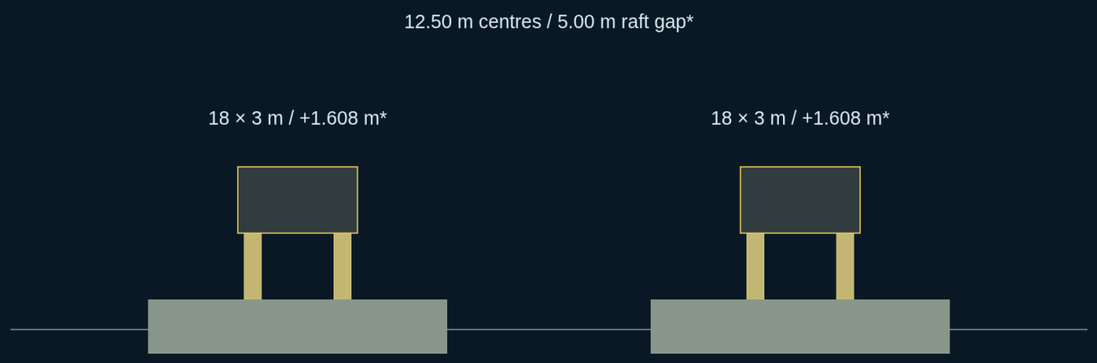

*Levels, raft and ramps are assumptions, not OEM foundation drawings.

Civil assumptions: 28 x 7.5 x 0.35 m raft; 100 mm pedestal; 100 mm mount; 308 mm module. OEM reinforcement, concrete grade, anchors and bearing design are not supplied. Verify settlement, flooding, drainage, corrosion and adjacent-foundation interaction before construction.

Element	Size / position	Status
Two static stations	2 × 80 t × 20 kg · nominal 18 × 3 m	Same instrument specification on each lane
Platform / overall width	18 × 3 m / 3.20 m	Nominal differs from drawing overall width; not clear width
Modules	6 × 1.50 × 6.00 × 0.308 m	2 across × 3 longitudinal; module depth is not plate gauge
Corridor / centres	22 × 170 m / 12.50 m	Coordination; excludes loop/holding/setbacks
Two raft concepts / gap	2 × 28 × 7.50 × 0.35 m / 5.00 m	Not OEM drawings; soil interaction unverified
Concept levels	Yard +0.900; raft +1.100; pedestal 0.100; mount 0.100; deck +1.608 m	Except 308 mm module, levels/supports are coordination assumptions
Concept ramps / landings	2 × 14.16 m @ 5%; 2 × 3 m; footprint 52.32 m	0.708 m rise; 4.5 m approach ramps to 3 m deck; taper needs OEM design
Rails / cells	12 × 75 × 2900 × 180 mm; 8 × 30 t	80 t system capacity; 8 × 30 t does not mean 240 t scale capacity
Directions	Entry X=-6.25, +Z / Exit X=+6.25, -Z	No crossing inside weighing corridor
Clearance / capacity	3.00 m nominal / 3.20 m overall / 80 t gross each	3.2 m mining profile held; overload does not produce a final net weight
Sensing	0 WIM / 0 quartz / 0 WIM IR / 2 CCTV / 2 QR	Position detection and safety gates remain required

OEM / civil

PDF does not provide foundation/ramp drawings, reinforcement, concrete grade, bearing or anchor details. Foundation drawing is supplied after PO.

Reclaimed soil / flooding

The simulated 28 × 7.5 × 0.35 m raft, levels and ramps are coordination assumptions. Check CPT/SPT, settlement, adjacent static interaction, drainage/flooding and excavation limits.

Truck / clearance

The 3 m nominal platform differs from the 3.2 m overall drawing width. A 3.2 m truck is on engineering hold until tyre positions, guard-rail clearance and swept envelope are approved.

Interface / AIMOC

FS-8000 ports/protocol, units, gross/tare/net modes, stable flag, checksum and software licensing are not supplied. IoT gateway is additional integration scope; Excel export is not a real-time API.

Metrology / FAT-SAT

Verify type approval for the installed variant, site verification and eccentricity/stability/repeatability tests and test loads. A 20 kg division is not a ±20 kg accuracy guarantee.

Environment / scope

Confirm 30 t cell IP/material, salt/flood protection and coating repair. PDF excludes foundation, ramps and weigh house; customer supplies power, cables and lifting equipment. Computer/verification scope needs clarification because the list and terms differ.

PDF schedule: 30-day fabrication if unavailable + 4 working days equipment installation; excludes civil/curing/integration/verification. Confirm PDF date/revision, 30 t cell IP, sensitivity, computer/verification scope and type-approval certificate.
